ID	Task Mode	Task Name	Duration	Start	Finish
1		CITGO KEROSENE PKGS	60 days	Tue 3/11/14	Mon 6/2/14
2		PO'S ISSUED			
3		**KEROSENE PKG 1**	**25 days**	**Tue 3/11/14**	**Mon 4/14/14**
4		Material order	1 day	Tue 3/11/14	Tue 3/11/14
5		Material Delivery	1 day	Thu 3/13/14	Thu 3/13/14
6		Off load materials	1 day	Fri 3/14/14	Fri 3/14/14
7		Pipe fitting	7 days	Mon 3/17/14	Tue 3/25/14
8		Welding	8 days	Wed 3/19/14	Fri 3/28/14
9		RT	2 days	Mon 3/31/14	Tue 4/1/14
10		Ship to Paint	2 days	Wed 4/2/14	Thu 4/3/14
11		Paint	4 days	Fri 4/4/14	Wed 4/9/14
12		PU at Paint	1 day	Thu 4/10/14	Thu 4/10/14
13		Ship to CITGO	2 days	Fri 4/11/14	Mon 4/14/14
14		**KEROSENE PKG 2**	**26 days**	**Fri 4/4/14**	**Fri 5/9/14**
15		Material order	1 day	Fri 4/4/14	Fri 4/4/14
16		Material Delivery	3 days	Mon 4/7/14	Wed 4/9/14
17		Off load materials	1 day	Thu 4/10/14	Thu 4/10/14
18		Pipe fitting	7 days	Fri 4/11/14	Mon 4/21/14
19		Welding	8 days	Mon 4/14/14	Wed 4/23/14
20		RT	2 days	Thu 4/24/14	Fri 4/25/14
21		Ship to Paint	1 day	Mon 4/28/14	Mon 4/28/14
22		Paint	5 days	Tue 4/29/14	Mon 5/5/14
23		PU at Paint	2 days	Tue 5/6/14	Wed 5/7/14
24		Ship to CITGO	2 days	Thu 5/8/14	Fri 5/9/14
25		**KEROSENE PKG 3**	**29 days**	**Fri 4/18/14**	**Wed 5/28/14**
26		Material order	1 day	Fri 4/18/14	Fri 4/18/14
27		Material Delivery	1 day	Mon 4/21/14	Mon 4/21/14
28		Off load materials	1 day	Tue 4/22/14	Tue 4/22/14
29		Pipe fitting	5 days	Mon 4/21/14	Fri 4/25/14
30		Welding	13 days	Wed 4/23/14	Fri 5/9/14
31		RT	2 days	Mon 5/12/14	Tue 5/13/14
32		Ship to Paint	2 days	Wed 5/14/14	Thu 5/15/14
33		Paint	5 days	Fri 5/16/14	Thu 5/22/14
34		PU at Paint	2 days	Fri 5/23/14	Mon 5/26/14
35		Ship to CITGO	2 days	Tue 5/27/14	Wed 5/28/14
36		**KEROSENE PKG 4**	**23 days**	**Mon 5/5/14**	**Wed 6/4/14**
37		Material order	1 day	Mon 5/5/14	Mon 5/5/14
38		Material Delivery	1 day	Thu 5/8/14	Thu 5/8/14
39		Off load materials	1 day	Thu 5/8/14	Thu 5/8/14
40		Pipe fitting	4 days	Fri 5/9/14	Wed 5/14/14
41		Welding	5 days	Mon 5/12/14	Fri 5/16/14
42		RT	2 days	Mon 5/19/14	Tue 5/20/14
43		Ship to Paint	2 days	Wed 5/21/14	Thu 5/22/14
44		Paint	5 days	Fri 5/23/14	Thu 5/29/14
45		PU at Paint	2 days	Fri 5/30/14	Mon 6/2/14
46		Ship to CITGO	2 days	Tue 6/3/14	Wed 6/4/14

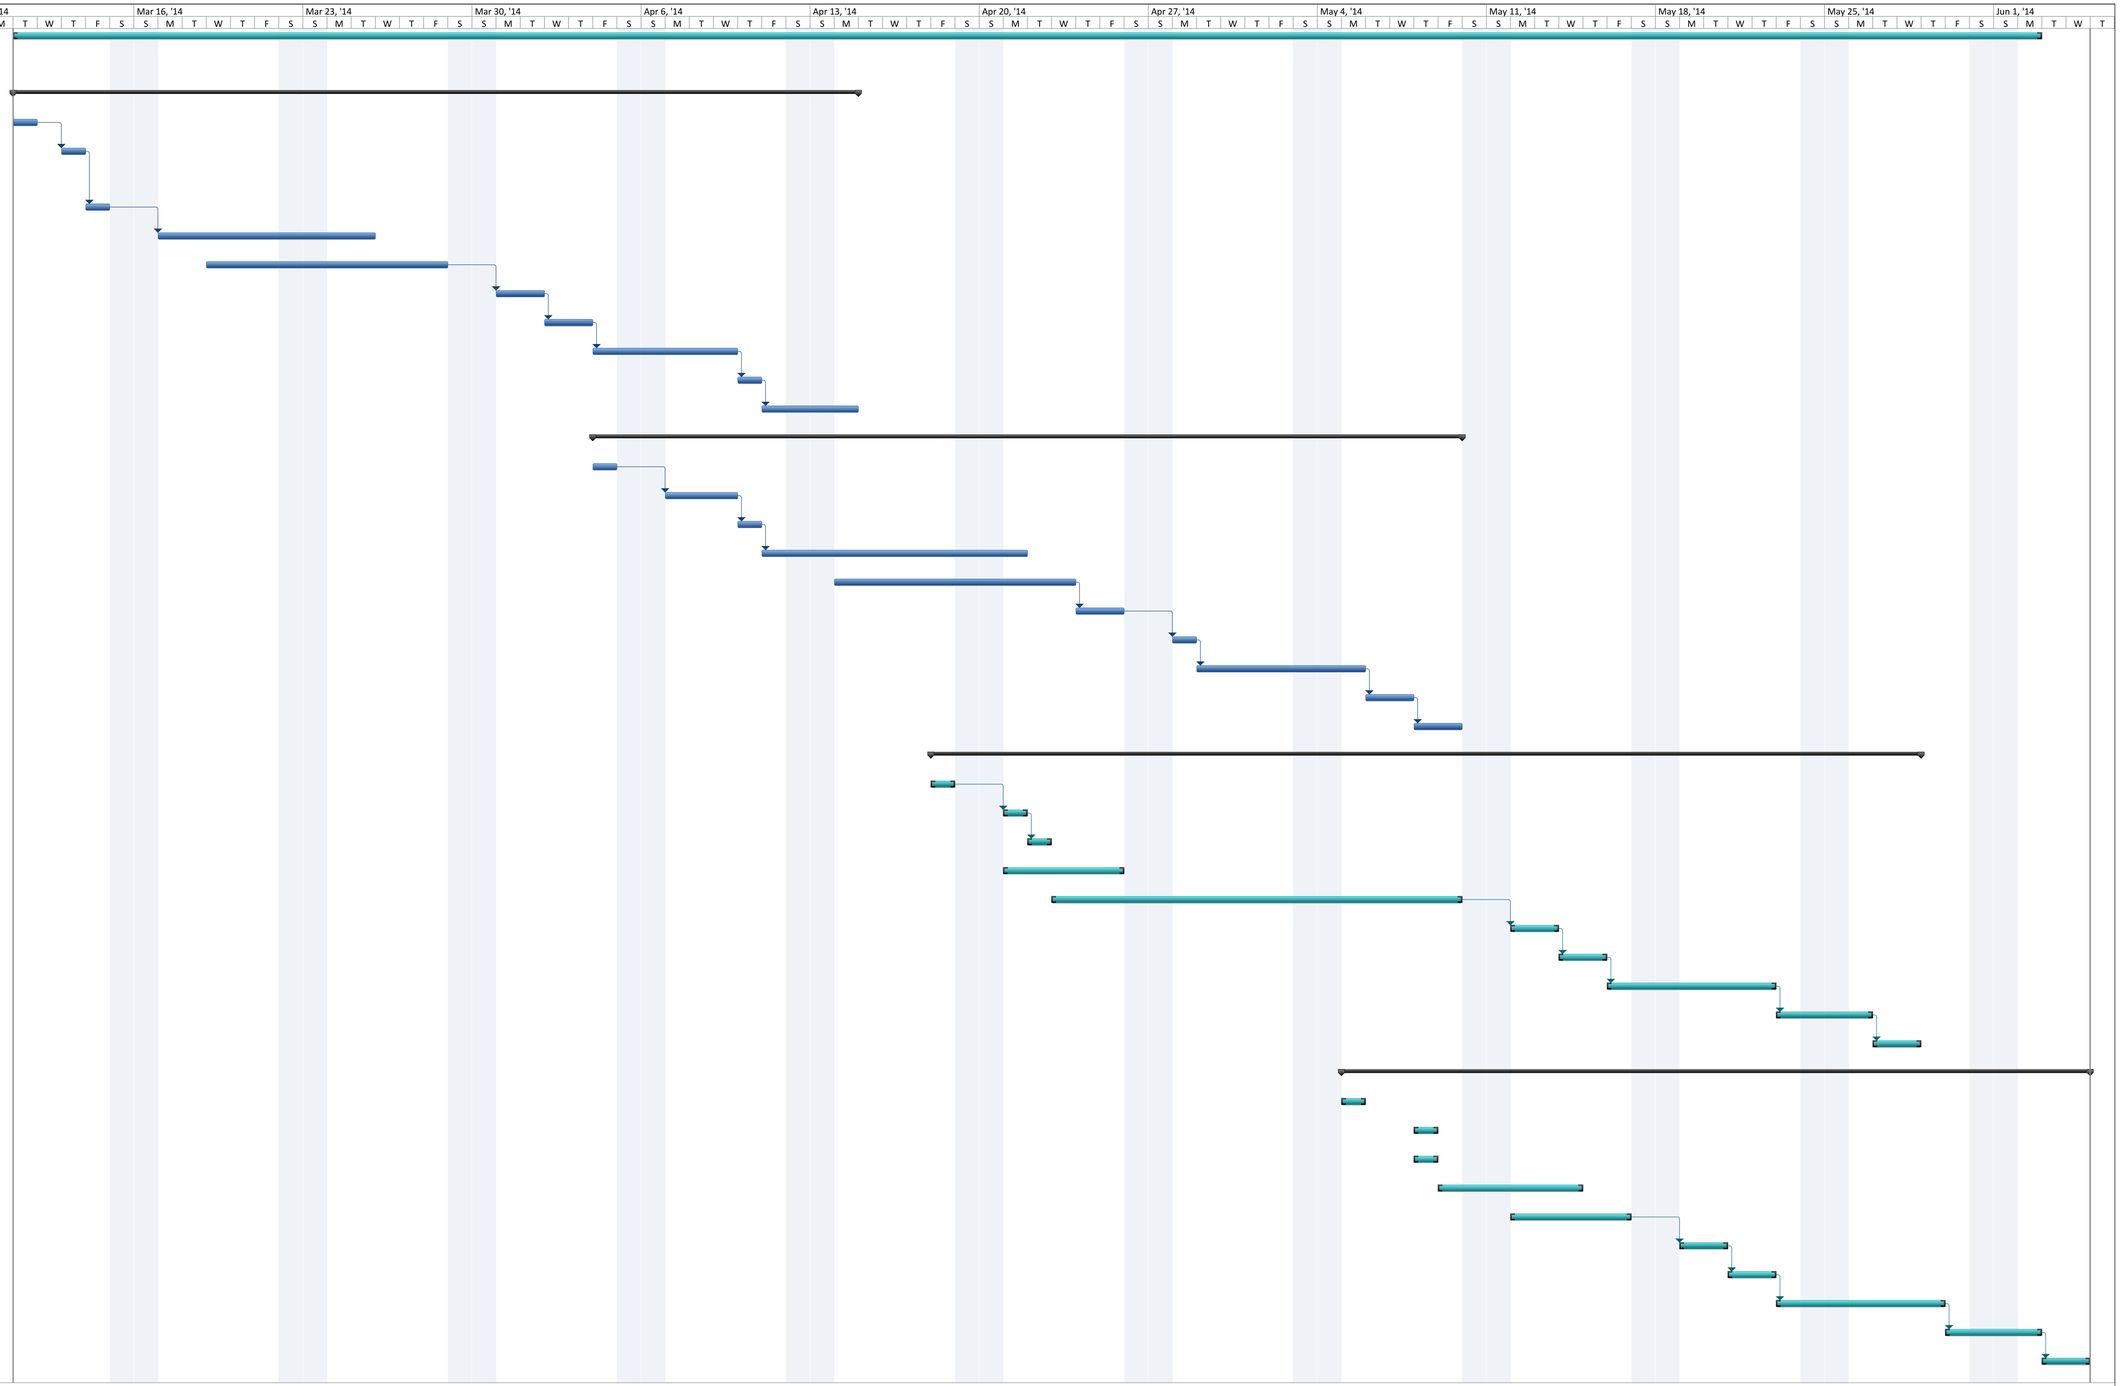

Project: CITGO KEROSENE.mpp
Date: Tue 3/11/14

Task | Milestone | Project Summary | External Milestone | Inactive Milestone | Manual Task | Manual Summary Rollup | Start-only | Deadline
Split | Summary | External Tasks | Inactive Task | Inactive Summary | Duration-only | Manual Summary | Finish-only | Progress
